10APPLES ARCHITECTURAL & PRODUCTION DIVISION

DWG NO: 10A-DWG-2026.4

FABRICATION WORK ORDER & TECHNICAL BLUEPRINT

Work Order #BX-2026-5716 • Model: **10FT Double-Wing Expandable House** (10.2' × 19.4')

CUSTOMER & PROJECT

Lazermouth Technologies

+233 0548619770

lazermouthtech@gmail.com

INSTALLATION SITE

120, Ayawaso West Municipal (East Legon / Dzorwulu / Airport Residential), Greater Accra Region, Ghana

Zip: GH-22992-21 • Land: Own Land

MANUFACTURING TIMELINE

Issued: 11/9/2026

Target Delivery: 2026-12-14

Plant 1, Bay C4

STATUS & VERIFICATION

DEPOSIT RECEIVED

Deposit: GH₵3,250 (Verified)

1.0 ARCHITECTURAL LINE DRAWINGS & ORTHOGRAPHIC BLUEPRINT


Model: 10FT Double-Wing Expandable House (3,100mm × 5,900mm × 2,500mm (Folded: 2,200mm))

ARCHITECTURAL LINE DRAWING & CAD BLUEPRINT | 10FT Double-Wing Expandable House | Active Plan: 2-bed-1-bath

All Views | Plan | Elevation | Foundation | CAD White


VIEW 1: ACTUAL SELECTED ARCHITECTURAL FLOOR PLAN & LIVING LAYOUT


DIMENSIONS: IMPERIAL & METRIC

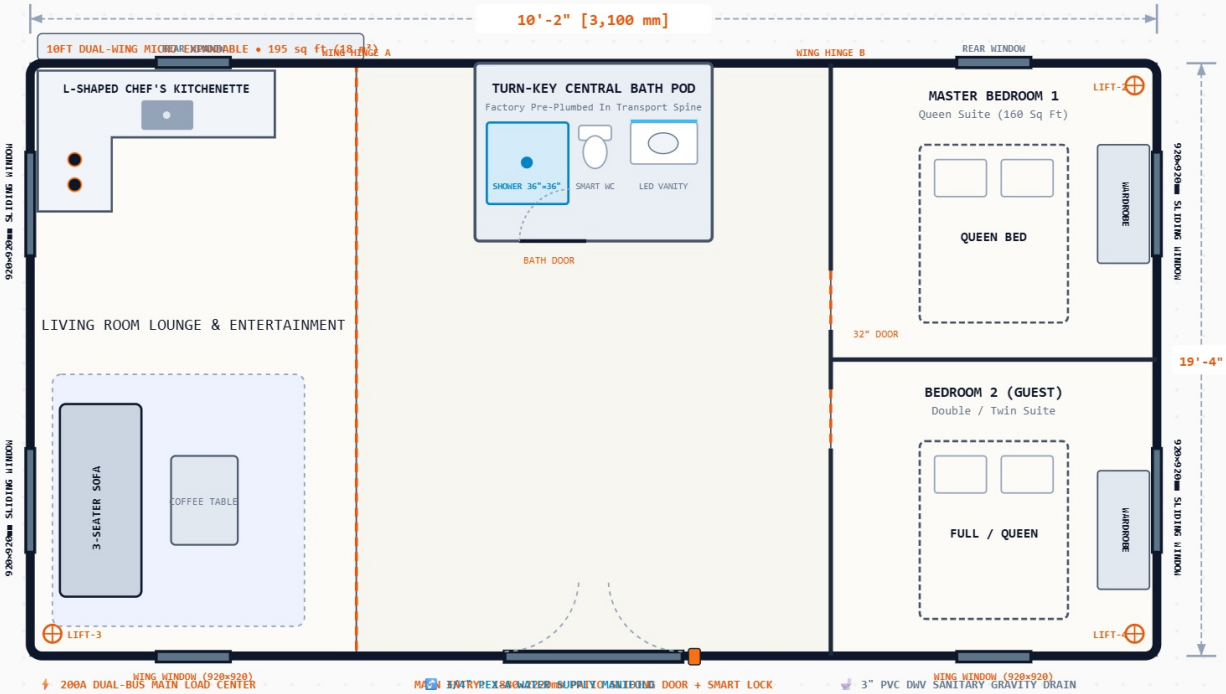


VIEW 2: FRONT EXTERIOR ORTHOGRAPHIC ELEVATION & RIGGING

WALL PANELS & CURTAIN GLASS

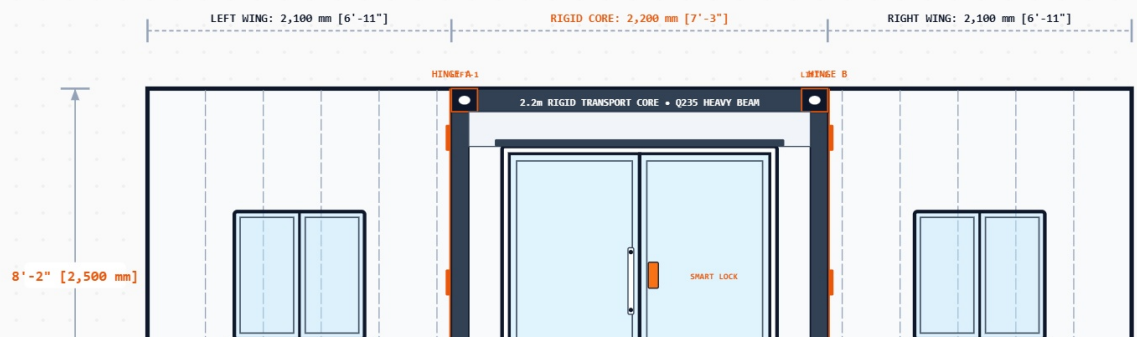

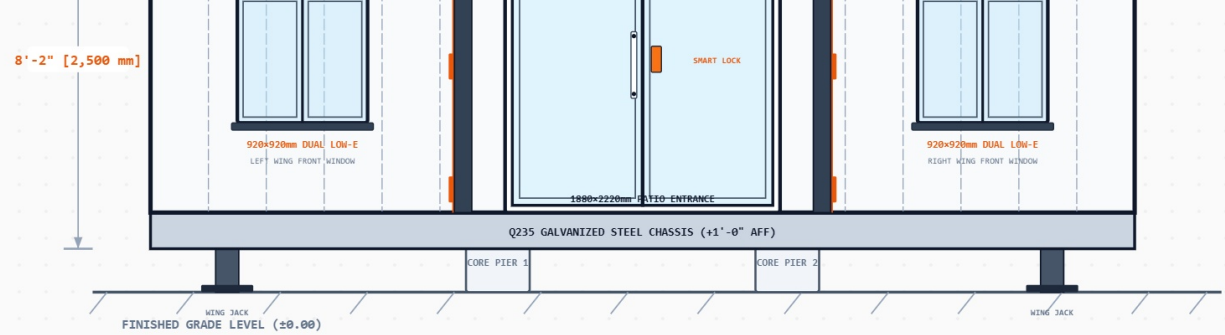

VIEW 3: STRUCTURAL FOUNDATION ANCHOR GRID & MEP ROUGH-IN — PIER BOLT LAYOUT & SERVICE INGRESS

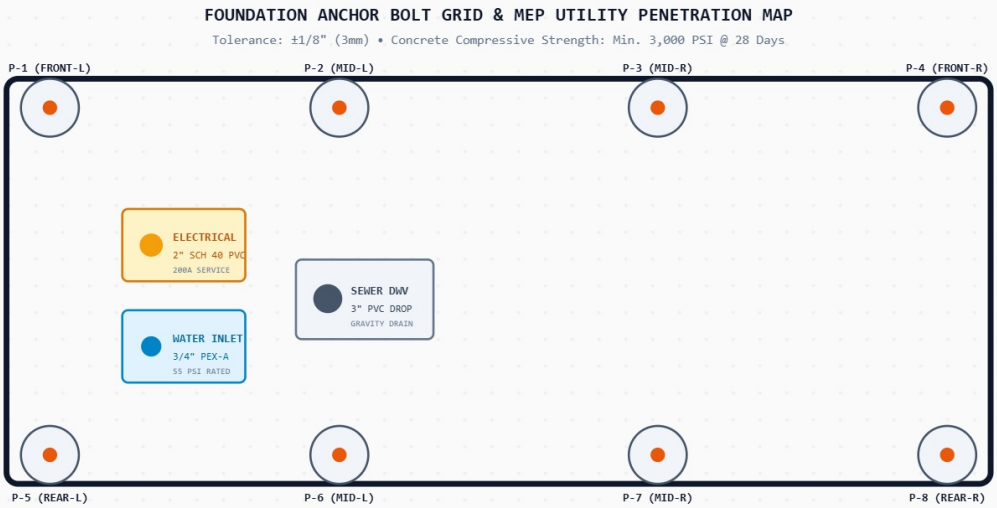

APPROVED FOR PRODUCTION: YES • AUTOCAD REV: 2026.4 • IBC & HUD CODE COMPLIANT • TOLERANCE: ±1/8" [3.2mm]

Engineering dimensions factory verified. All rights reserved.

2.0 PHYSICAL MEASURES, CLEARANCES & RIGGING SPECIFICATIONS

Engineering Precision Tolerance: ±1/8" (3.2mm)

OVERALL EXTERIOR FOOTPRINT
10.2'-0" L × 19.4'-0" W × 8.2'-0" H
3,100mm × 5,900mm × 2,500mm (Folded: 2,200mm)

USABLE INTERIOR LIVING SPACE
195 SQ FT [18.1 m²]
Clear Ceiling: 8'-6" [2,590 mm] AFF

DRY TARE WEIGHT & CRANE RIG
23,800 LBS [10,795 KG]
4x ISO Corner Twistlock Castings

STRUCTURAL LOAD RATINGS
140 MPH Wind • 40 PSF Snow
Seismic Zone D • Flame Spread Class A

Foundation Pier & Anchor Bolt Schedule (10-Point Foundation Support)

Min. 3,000 PSI Concrete

PIER TYPE & SIZING
12" Ø Concrete Pier or Helical Pile to frost depth

ANCHOR BOLT HARDWARE
2× 5/8" ASTM A307 HDG bolts per pier, 8" embedment

SOIL BEARING CAPACITY
Min. 2,000 PSF undisturbed bearing capacity

3.0 CUSTOM ENCLOSURE & ARCHITECTURAL MATERIALS BILL (BOM)

Verified Against Customer Reservation Dossier

CATEGORY	SELECTED SPECIFICATION & MATERIAL	TECHNICAL DETAILS / RATING	STATUS
Exterior Skin	Crisp White Plate	Fluorocarbon coated alloy, R-24 polyiso core, fire-retardant Class A	Allocated
Glazing Envelope	Broken bridge aluminum sliding door	Dual 6mm+12A+6mm tempered Low-E argon insulated, U-factor 1.4, STC 40dB	In Stock
Flooring Core	Luxury SPC Nordic Pale Oak	Rigid core waterproof SPC plank (7.5mm), IXPE 1.5mm acoustic underlayment	Allocated
Kitchen	Matte Black Soft-Touch	Quartz composite slab counter, Blum soft-close European hardware	Ready

Flooring Core	**Luxury SPC Nordic Pale Oak**	Rigid core waterproof SPC plank (7.5mm), IXPE 1.5mm acoustic underlayment	Allocated
Kitchen Millwork	**Matte Black Soft-Touch**	Quartz composite slab counter, Blum soft-close European hardware	Ready
Roof & Solar	**Standard Integrated Parapet Flat Roof**	TPO/EPDM membrane, 1.5° drainage pitch, pre-wired conduit to inverter hub	Allocated
Electrical Hub	**Pre-Wired 100A Factory Service Center**	200A 120/240V Dual-Bus, copper romex wiring, AFCI/GFCI breakers throughout	Verified
Lighting Package	**Architectural Recessed LED Downlights**	24V COB linear architectural indirect LED glow, CRI 95+, 3000K warm white	In Stock

FACTORY PRE-INSTALLED MODULAR ADD-ONS & ACCESSORIES:

- Integrated Waterproof Bath Pod (10FT Micro Bath Pod (1.3m Run))
- L-Shaped Modular Kitchen Cabinet (10FT Micro "L"-Shaped Kitchenette (1.45m Run))
- Front Entry Modular Pergola & Patio Deck (10FT Compact Patio Deck (120 sq ft))

4.0 MEP FACTORY UTILITY ROUGH-IN & CONNECTION SCHEDULE

Plug-and-Play Quick-Connect Ports

Electrical Ingress & Breakers

- Main: **200A 120/240V Dual-Bus**
- Ingress: 2" PVC stub-up @ rear left corner
- C1: 20A Kitchen Small Appliance (GFCI)
- C2: 20A Induction Cooktop (240V dedicated)
- C3: 20A Bath Pod GFCI & Exhaust Fan
- C4: 25A 240V HVAC Mini-Split circuit
- C5: 15A Architectural Lighting & USB outlets

Water Supply & Drainage

- Fresh Water: 3/4" PEX-A with brass shutoff
- Location: +18" AFF chassis rear wall
- Pressure Rating: 55–65 PSI operating range
- Hot Water: 13.5kW 240V on-demand tankless
- Sewer Drain: 3" **DWV PVC** cleanout drop
- Drain Ingress: 6" below finished chassis base
- Vent: 1-1/2" stack with flashing collar

Climate Control & Ventilation

- Mini-Split: **24,000 BTU Multi-Zone Dual-Head**
- Line-Set: 3/8" liquid + 5/8" suction pre-run
- Sleeve: 3" thru-wall collar @ +84" AFF
- Condensate: 3/4" gravity drain to grade
- Exterior Bracket: Heavy-gauge powder coated
- Bathroom ERV: 80 CFM continuous cycle
- Range Hood: 250 CFM recirculating / exterior

5.0 PROJECT INVOICING & FINANCIAL LEDGER

Single Currency Enforced: GHS

BASE CABIN CHASSIS	OPTIONS & UPGRADES	FREIGHT & SITE PREP	TOTAL CONTRACT VALUE
GH₵192,400	GH₵0	GH₵10,000	**GH₵78,205**

6.0 SHOP FLOOR FABRICATION & PRE-DISPATCH QA INSPECTION CHECKLIST

Completed: 6 / 10 Steps

Lead technician must verify and stamp each checkpoint before rolling unit to transit packaging.

- [x] **1. Q235 steel chassis diagonal squareness verified within ±1/8" (3mm)**
- [x] **2. All structural framing weld seams inspected & magnetic particle tested**
- [x] **3. Foundation anchor bracket bolt torques certified to 120 ft-lbs**
- [x] **4. External envelope rain deluge spray test completed (30 mins @ 35 PSI)**
- [x] **5. Electrical load center Megger insulation & dielectric ground test passed**
- [x] **6. PEX supply pressure decay test passed (100 PSI air, 24-hour hold)**
- [ ] 7. Low-E panoramic glazing weather-stripping & window locks inspected
- [ ] 8. Quartz kitchen counter & bathroom vanity plumbing fixtures leak-free
- [ ] 9. Mini-split heat pump line-set vacuum pulled below 500 microns
- [ ] 10. Crane pick lugs load-tested to 45 kN and transit shrink-wrap applied

LEAD ASSEMBLY ENGINEER

Marcus Sterling, PE #48291

Signature on File • Plant Operations

QUALITY CONTROL INSPECTOR

Sarah Jenkins, CWI

Certified Welding & Code Inspector

10APPLES QC
PASSED
DISPATCH OK

Serial Tag #10A-2026-MFG

Marcus Sterling, PE #48291

Signature on File • Plant Operations

Sarah Jenkins, CWI

Certified Welding & Code Inspector

PASSED
DISPATCH OK

Serial Tag #10A-2026-MFG
